

04-04-16



- CLUSTER C:**
- C1, C2: Outer plastering work completed.
  - C3 & C4: Outer and Inner plastering work completed.
  - C5 : Inner plastering work under progress.
  - C6 : Roof RCC Work completed.

04-04-16



**CLUSTER D:** D1 to D4 & D6 :Outer and Inner plastering work completed.  
D5 : Outer Plastering work completed.

04-04-16



H1 : Basement block work under progress.

H2 : Basement filling work completed.

H3 : plot marking work under progress.

H4 to H7 & H10 TO H 13: Basement level gravel filling work completed

H7A : Kept on Hold.

H9 : Basement block work completed.

H10 to H13: Basement gravel filling work in progress.

H14 : Footing PCC Work completed.

**CLUSTER H:**

04-04-16



**CLUSTER I:**

I4 & I5 : Lintel Level ?Block work under progress.  
I1,I2,I3,I21 & I22 : Kept on Hold.

04-04-16



**CLUSTER J:**

**J1&J2 : Basement block work under progress.**

**J3 : Basement filling work completed.**

**J4 & J7A: Lintel Bar Bending and Shuttering under progress.**

**J9 to J10 : Basement gravel filling work completed.**

04-04-16



**CLUSTER N:** N1 to N3 & N5 to N10: Outer and Inner Plastering work completed,  
painting and plumbing work under progress.  
N4 & N11 : Kept on Hold.

04-04-16



O1, O11, O12 & O14 : Outer & Inner Plastering work under progress.

O2, O3 & O13 : Roof RCC Work Completed..

O4, O5, O7 to O10 : Outer and Inner Plastering work Completed and Plumbing work under progress.

O6 : Lintel Bar Bending and Shuttering work Completed..

**CLUSTER O:**

04-04-16



**CLUSTER P:** P1to P6 : Outer & Inner plastering work completed.  
P7 to P10 : Plumbing work under progress.

04-04-16




**CLUSTER Q:** Q1 to Q4 : Outer & Inner Plastering work under progress  
Q5 to Q7A : Outer and Inner Plastering work completed

04-04-16



**CLUSTER R: R7A&R9: Plinth beam bar bending work under progress  
R4 & R5 : Model Villa.**

04-04-16

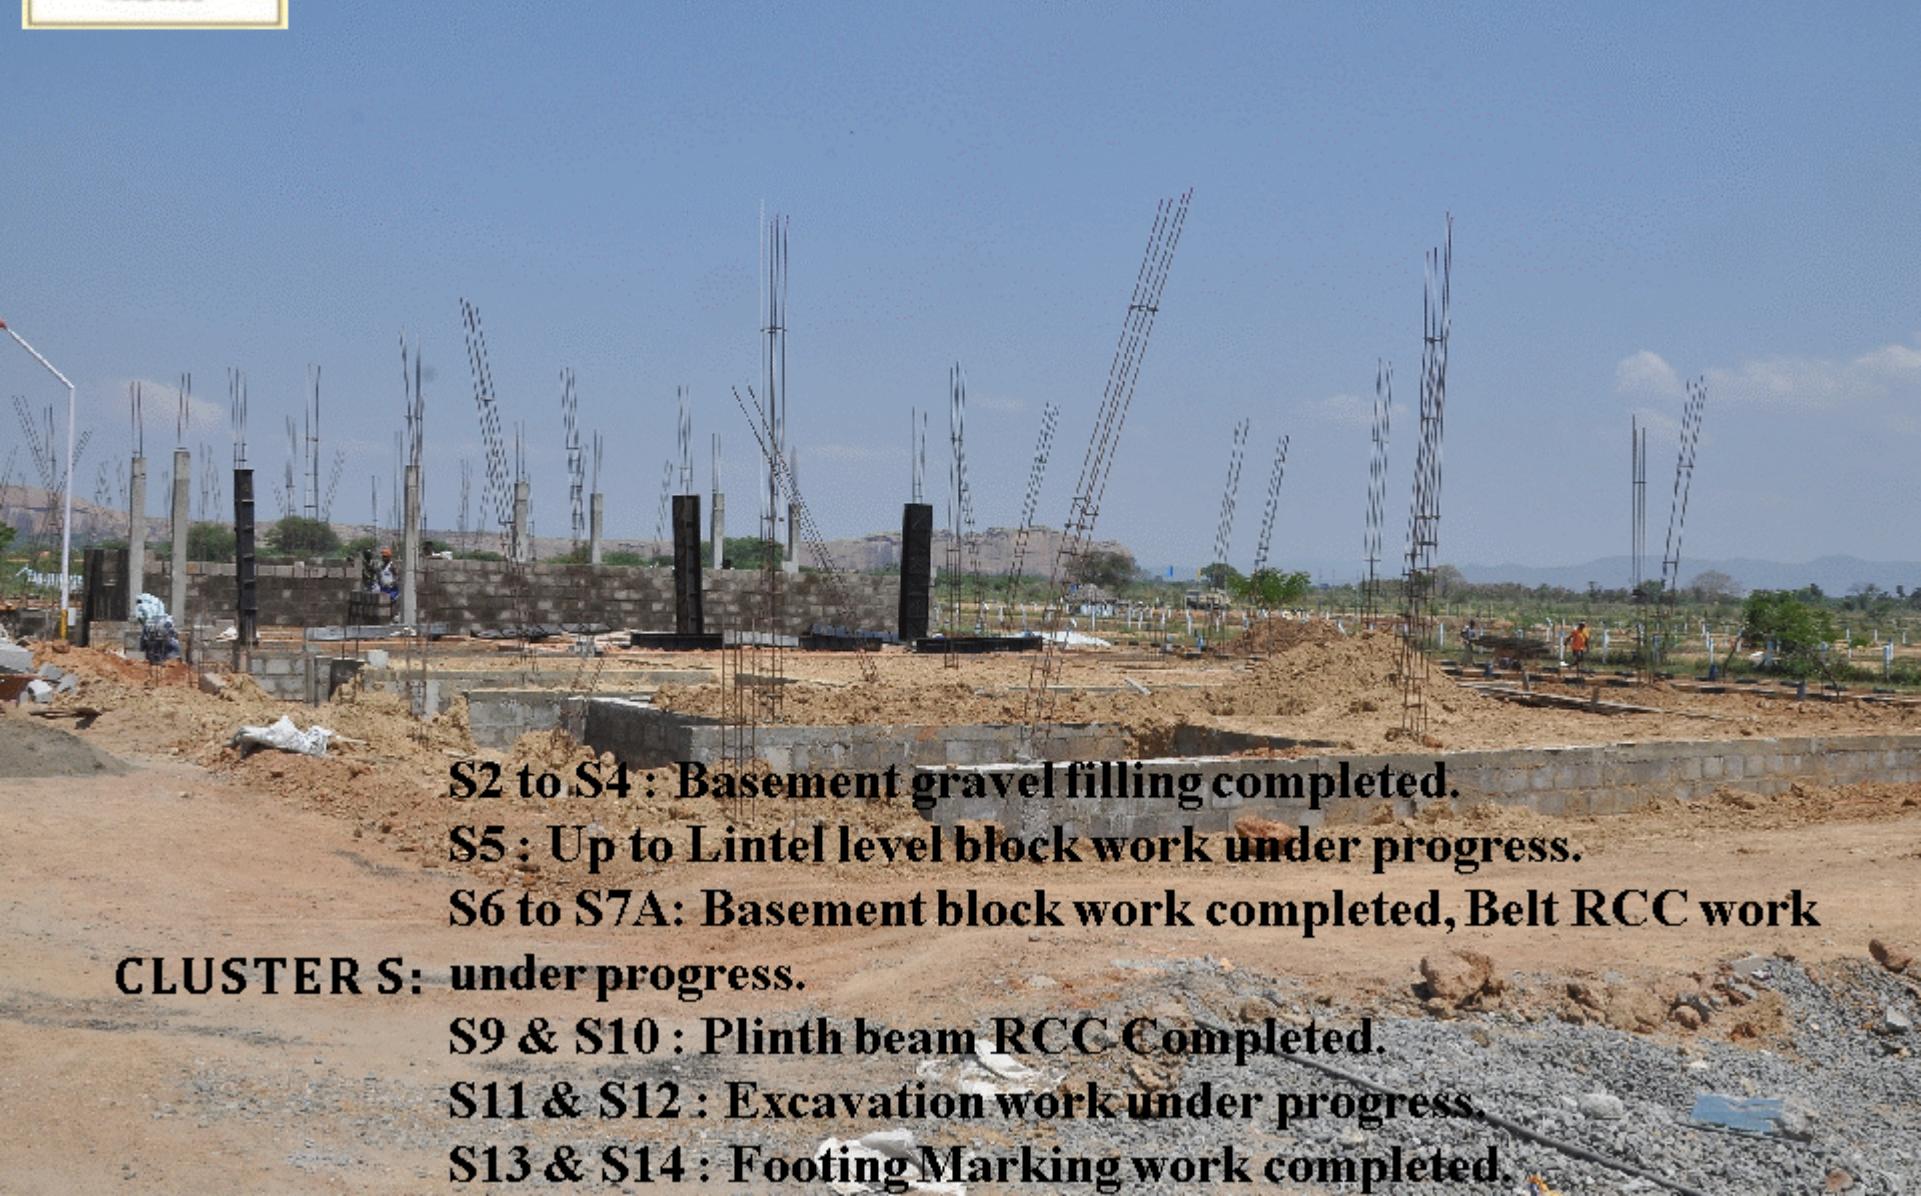

**S2 to S4 : Basement gravel filling completed.**

**S5 : Up to Lintel level block work under progress.**

**S6 to S7A: Basement block work completed, Belt RCC work**

**CLUSTER S: under progress.**

**S9 & S10 : Plinth beam RCC Completed.**

**S11 & S12 : Excavation work under progress.**

**S13 & S14 : Footing Marking work completed.**

04-04-16



U1 & U2 : Lintel level Block Work Completed..

**CLUSTER U:** U3 to U5 : Roof level block work completed, Roof slab bar bending and shuttering work under progress.

04-04-16



**CLUSTER V:** V1 & V2 : Roof pipe Laying & Bar bending work in progress.  
V3 & V4 : Basement Filling work completed.

04-04-16



W1 & W2 : Lintel level block work completed.

**CLUSTER W:** W3 & W4 : Kept on Hold.

04-04-16



X1 & X2 : Plinth Beam RCC work under progress..

**CLUSTER X:** X3 & X6 : Footing RCC Work under progress

X4, X5 & X7 : kept on Hold.
