

30-03-16



C1, C2 & C25: Roof RCC completed.


**CLUSTER C:** C3 & C4: Outer and Inner plastering work completed.  
C6: Roof Level block work completed.

30-03-16



**CLUSTER D:** D1 to D4 & D6 :Outer and Inner plastering work completed.  
D5 : Outer Plastering work completed.

30-03-16

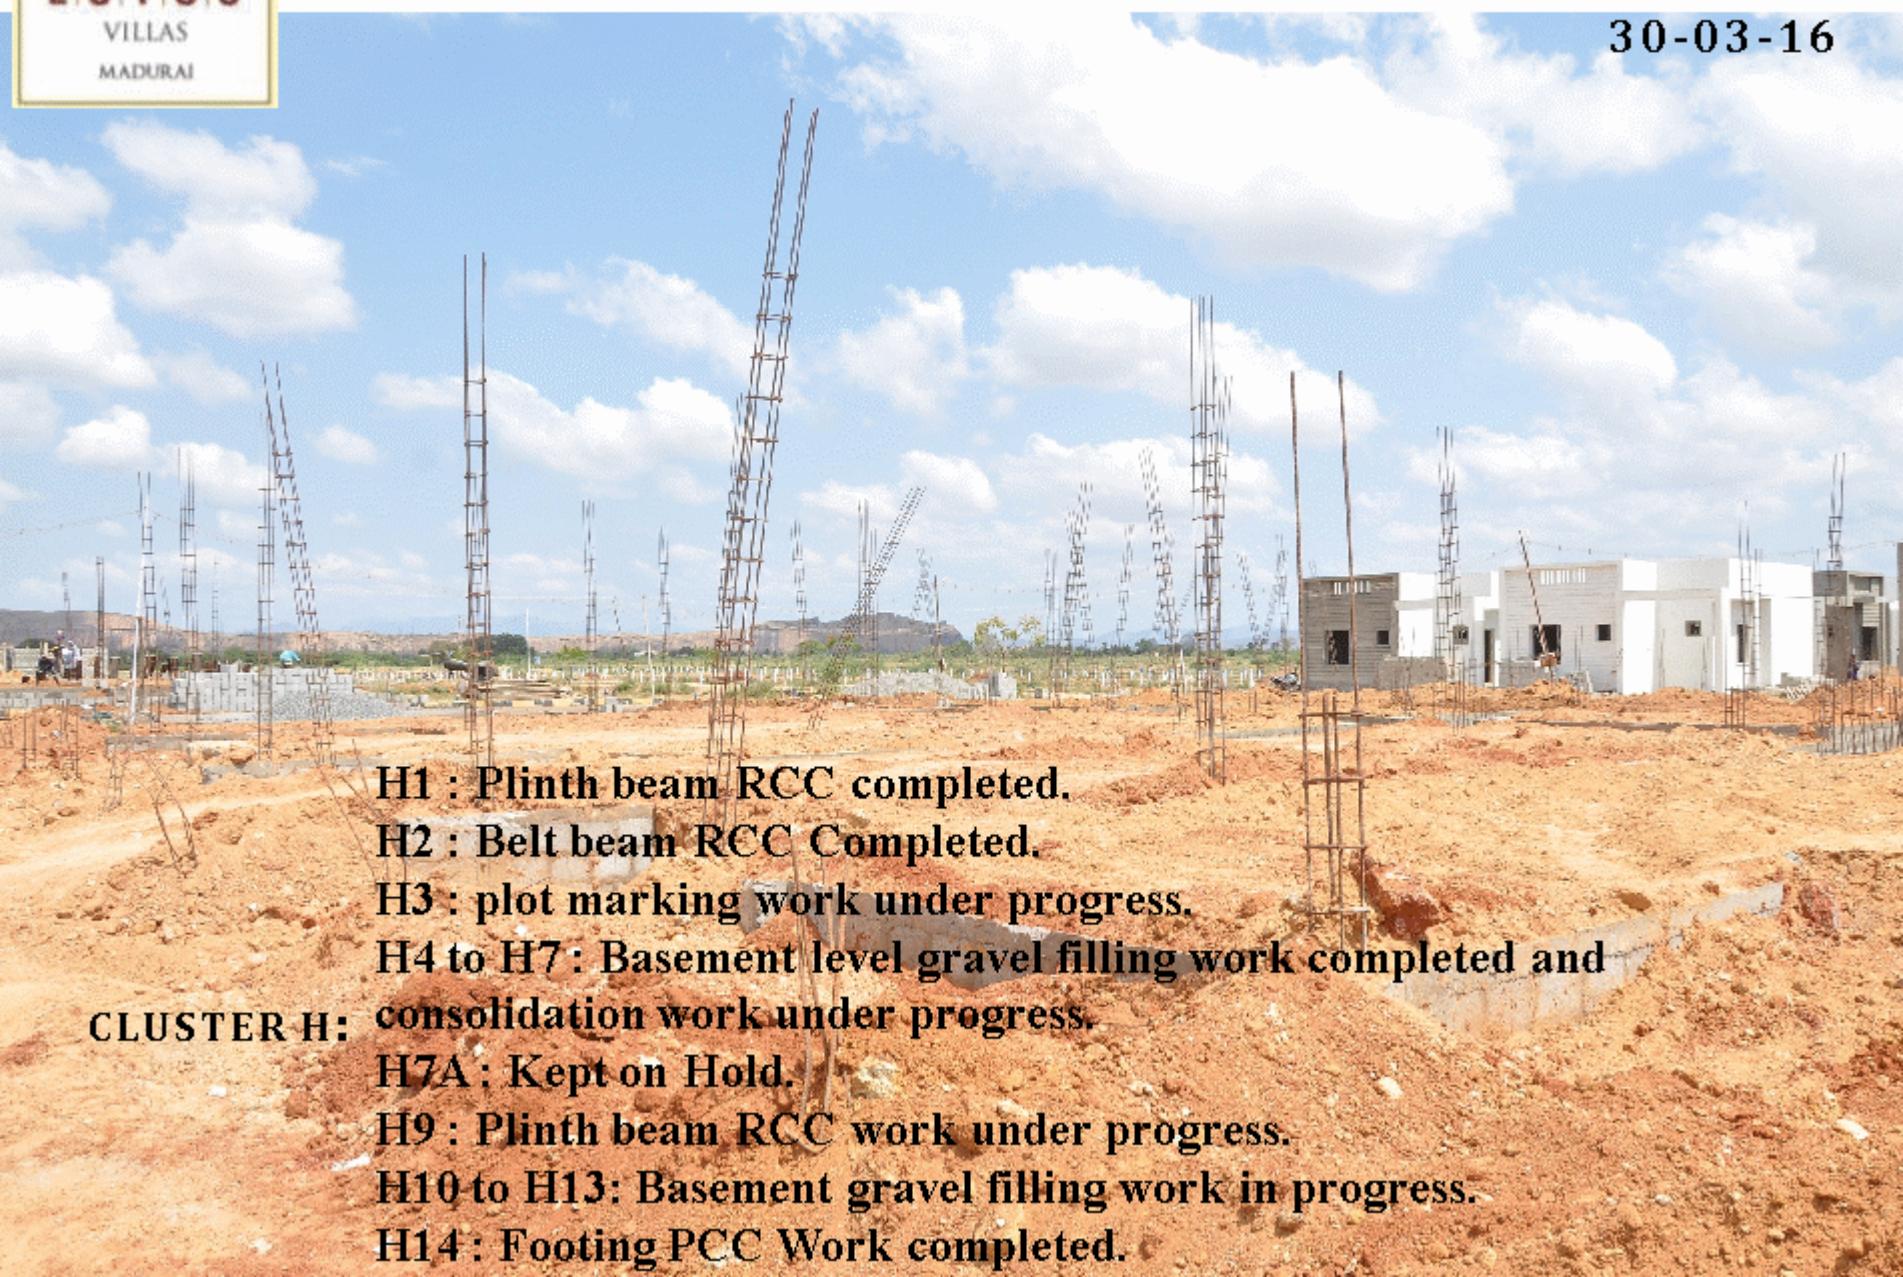

**H1 : Plinth beam RCC completed.**

**H2 : Belt beam RCC Completed.**

**H3 : plot marking work under progress.**

**CLUSTER H:** **H4 to H7 : Basement level gravel filling work completed and consolidation work under progress.**

**H7A : Kept on Hold.**

**H9 : Plinth beam RCC work under progress.**

**H10 to H13: Basement gravel filling work in progress.**

**H14 : Footing PCC Work completed.**

# VNCT LOTUS VILLAS SITE PICS


30-03-16



**CLUSTER I:**

I4 & I5 : Basement gravel filling under progress  
I1,I2,I3,I21 & I22 : Kept on Hold.

30-03-16

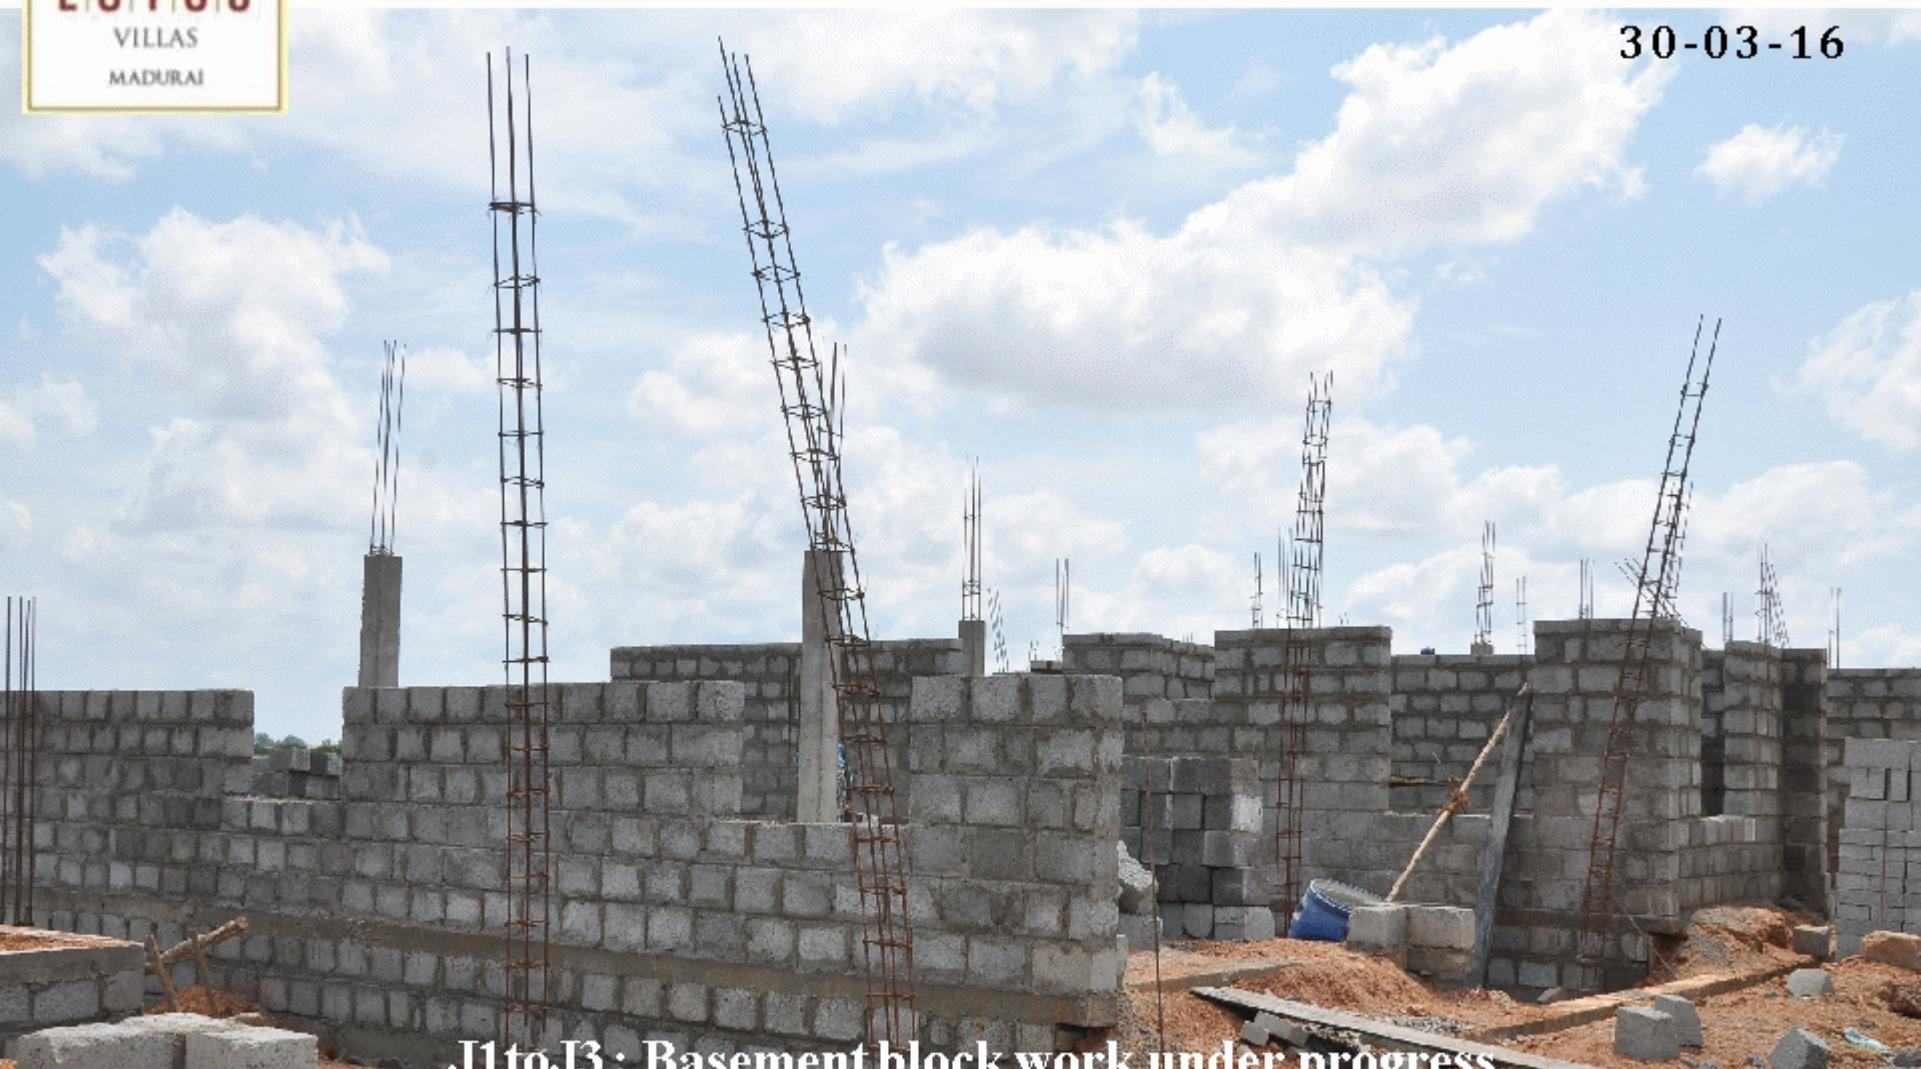

**J1toJ3 : Basement block work under progress.**

**J4 & J5 : Lintel Level Block work completed.**

**J6 & J7 : Lintel level block work under progress.**

**J7A to J10 : Basement gravel filling work completed.**

**CLUSTER J:**

30-03-16



**CLUSTER N:** N1 to N3 & N5 to N10: Outer and Inner Plastering work completed and plumbing work under progress.  
N4 & N11 : Kept on Hold.

30-03-16



O1 to O3, & O12 to O14 : Roof RCC completed.

**CLUSTER O:** O4,O5,O7,O7A, O9,O10 &O11:Outer and Inner plastering work completed.

O12 : Outer and Inner Plastering work under progress.

O6 : Lintel level block work completed.

30-03-16



CLUSTER P:

P1to P5 : Outer & Inner plastering completed, plumbing work under progress.

P6 to P10 : Outer and inner plastering work under progress.

30-03-16



Q1 to Q4 : Outer Plastering work under progress

**CLUSTER Q:** Q5 to Q7 : Outer and Inner Plastering work completed

Q7A : Outer plastering work completed.

30-03-16



**CLUSTER R: R7A&R9: Plinth beam bar bending work under progress**

30-03-16



S2 & S3 : basement level Belt Beam RCC work completed.

S4 & S5 : basement filling work completed.

**CLUSTERS:** S6 : Plinth beam RCC work completed.

S7 : Plinth Beam Marking work under progress

S7A to S10 : Plinth beam excavation work & bar bending work under progress.

30-03-16



**CLUSTER U:** U1 & U2 : Lintel level Block Work Completed.  
U3 to U5 : Lintel RCC work completed.

30-03-16



**CLUSTER V:** V1 & V2 : Above lintel level block work completed.  
V3 & V4 : Basement level completed and Column RCC up to Roof level Completed.

30-03-16



W1 & W2 : Super Structure block work under progress.

**CLUSTER W:** W3 & W4 : Kept on Hold.

30-03-16



**CLUSTER X:** X1, X2, X3 & X6 : Excavation work completed.  
X4, X5 & X7 : Earth work, Excavation Under Progress
